



# Nevada Shared Radio System Update

P25 Technical Advisory Committee


March 18, 2021



# System Implementation Schedule

## Project Schedule

- Project kick-off: **November 2018**
- Region 0 Network Switching Center Install completion: **January 2020**
- Region 2 Design Phase: **In Progress**
  - Expected Completion **May 2021**.
- Washoe County site development/construction: March 2020 → **September 2022**
- Washoe County P25 Radio System Installation: June 2021 → **October 2022**
- Region 2 installation complete, cutover and acceptance: **May 2023**
- Final statewide system acceptance: **April 2024**

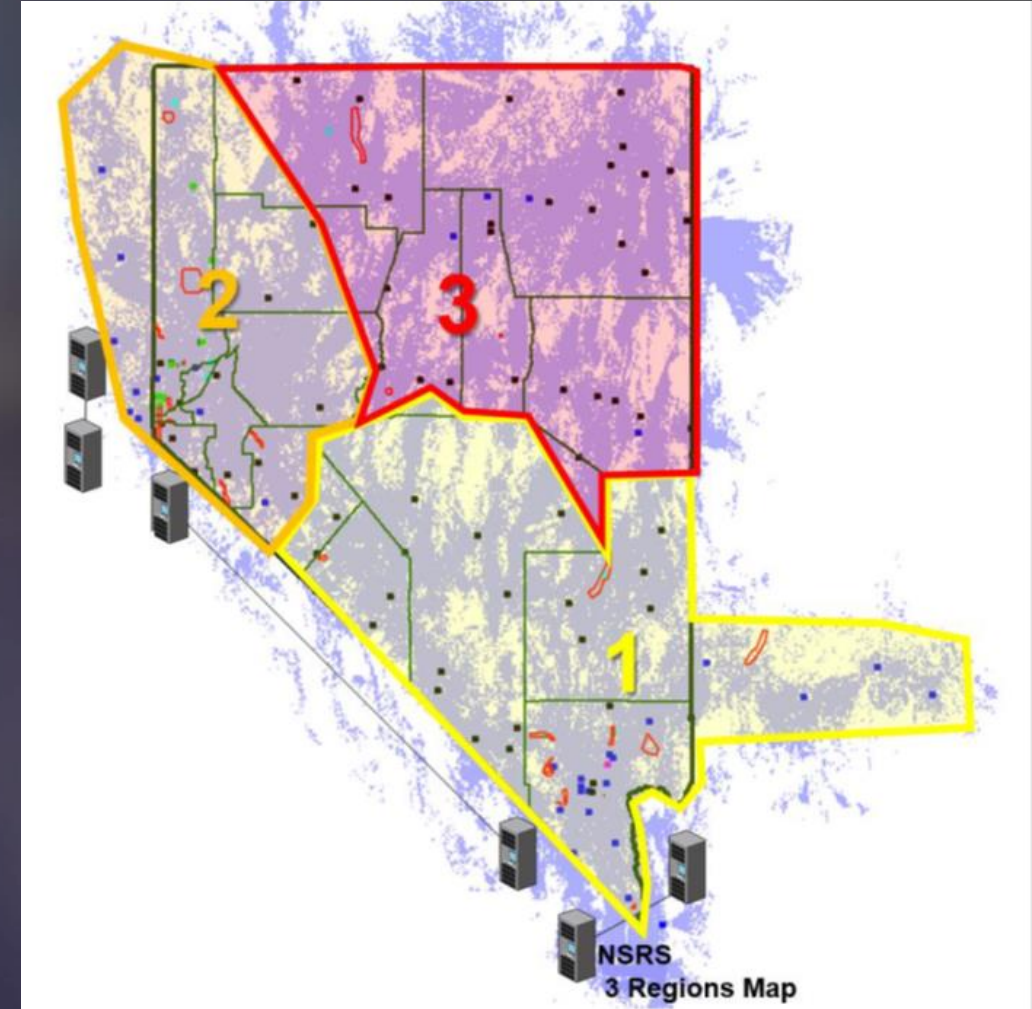





# Current Project Activities

- Detailed Design Review (DDR) underway (60% complete)
  - Review of 13 System level documents
  - 20 Site Design Packages (5 Greenfield sites)
- NSRS P25 Schedule not fully vetted
  - NSRS partners are working with System Integrator to develop a complete system deployment schedule.
- Greenfield site construction has been pushed off until Summer 2022
  - Moratorium on processing new requests through 3/21/2021 per Secretary of Interior Order#3395



# Questions?

Quinn Korbulic

[qkorbulic@washoecounty.us](mailto:qkorbulic@washoecounty.us)

775-328-2348



