



P25 JOC Meeting

October 19th, 2023



Nevada Shared Radio System Project Update

Agenda Item #7




Dispatch Console Upgrades

- Dispatch Consoles needed to be upgraded from Window 8.1 to windows 10.
- L3Harris will upgrade these consoles January through March 2024.
- Project Manager Dave TerMorshuizen from Federal Engineering will be filling in while Washoe County Communication Coordinator is out on medical.
- Dave will travel out to Washoe County the week of November 27th through December 1st to meet with all stakeholder and see all center. A Plan will be created and distributed to all team members, prior to medical leave start.

Tentative Dispatch Console Schedule

- Airport Dispatch
 - January 15th through 18th
- Washoe County School District
 - January 19th through 22nd
- Washoe County Court Complex
 - January 24th through January 26th
- Washoe County Detention Center
 - January 29th, through January 31st
- City of Sparks Dispatch
 - February 1st through 5th
- Washoe County Sheriff's Dispatch
 - February 2nd through February 18th
- City of Reno Dispatch
 - February 19th through February 26th

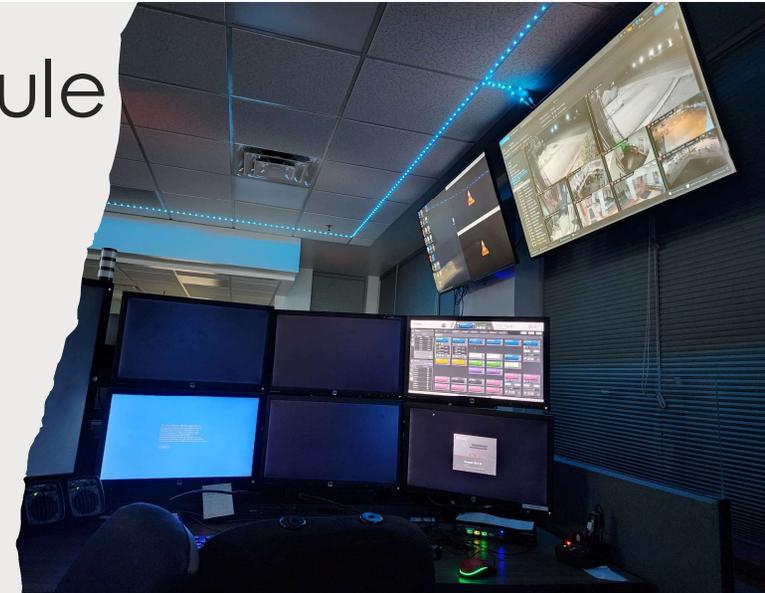



NSRS Radio System Update

- **Mobile Installations**

- **WCSO, WC Fire, WC CSD**

- 9/18-10/6

- **PLIC: DEM, PD Programming**

- 10/9-10/13

- **City of Reno: (Rob Allen)**


- 11/16/23-1/17/24

- **TMFPD**

- 1st Quarter 2024

- **Sparks Police Department**

- 1st quarter 2024

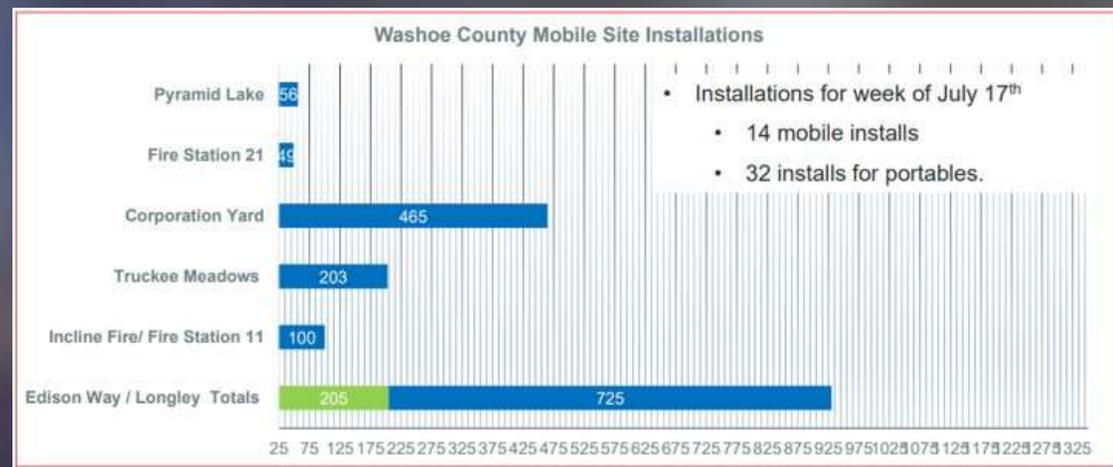

Step 1: meet with Radio Shop to standardize radio personality (DON THORBERRY)

Step 2: Verify all features on radios

Step 3: Have radios delivered to Radio Shop, or to designated location.



Cold Springs Construction Status
Cold Springs is 95% complete. WCRCS are waiting for the final punch list remediations from L3HARRIS team to complete the final walk-through.




Marble Bluff Construction Status

- Communications on Wheels Installed
- Old Tower Removed
- New Tower Installed
- Building Installed
- Driveway Expanded
- Conduits being installed for Fiber
- Waiting on Power from NVE to new building.



Tribal Approval Needed

- Need NVE Right of Way agreement signed by the tribe.
- Need approval for new secondary transformer design

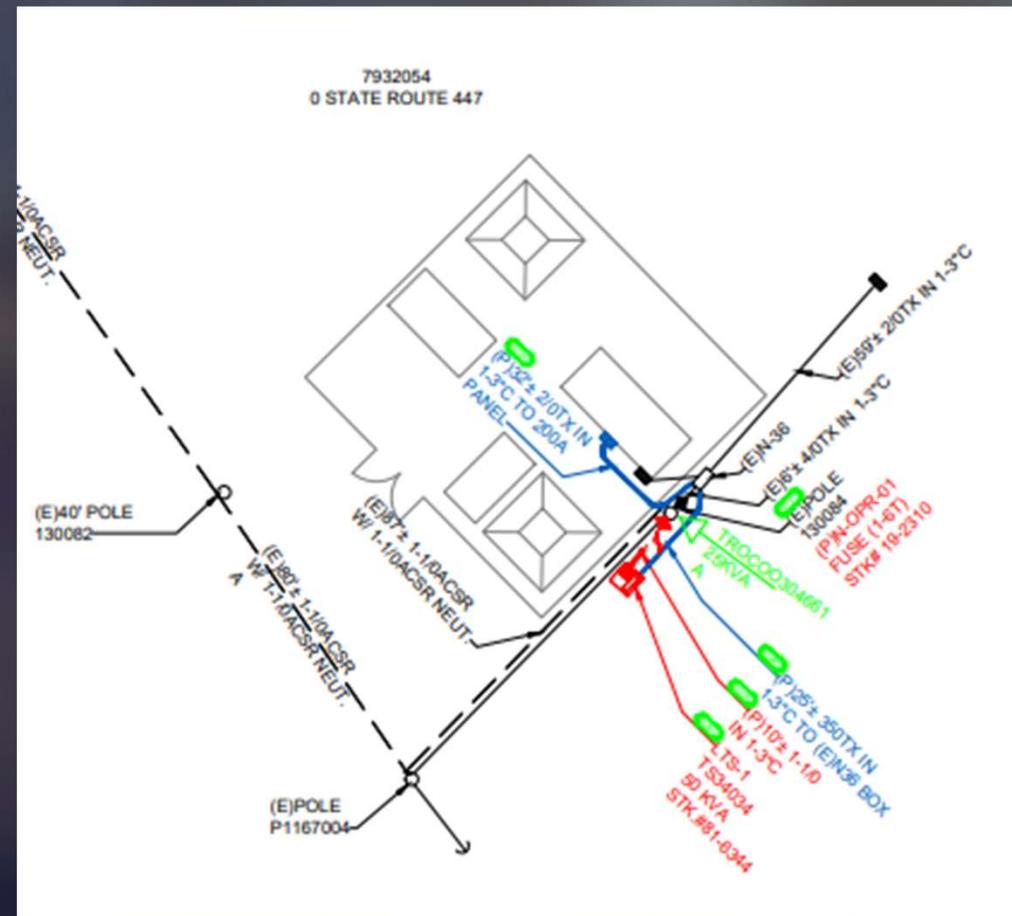



P25 Site Construction Updates

- P25 Line/Antenna and Rack installations
 - Slide 10/22
 - Peavine 7/23
 - Snowflake 10/23
 - Fox 10/23
 - Virginia Peak 10/23
 - Incline 11/23
 - Marble 10/23
 - Poito 5/24
 - Mt. Rose 7/24
 - Red Peak 5/24
 - Ashfields 6/24
 - SMOKEY QUARTZ & SEVEN LAKES pending BLM approvals.





800MHz Users Committee Member/Staff Announcements

Agenda Item 9



Announcements

- Melissa Lawney will be going out on FMLA leave effective December 12th, 2023 for approximately 2-3 months.
 - Regional Services Contacts
 - Quinn Korbolic-(775) 328-2348
 - WCRCS Contacts: (775) 858-5961
WCRCS@washoecounty.gov
 - John Byerly: (775) 741-5282
 - John Rees: (775) 433-3509
 - Tyler Gerber-Winn: (775) 444-2467
 - James Davis:(775) 530-2036
 - Radio Shop Contacts:
radioshopdl@washoecounty.gov
 - Don Thornberry: (775) 858-5953
 - Daniel Bale: (775) 858- 5962
 - Daniel Foster: (775) 858- 5962





Questions?

Melissa Lawney

Mlawney@washoecounty.gov

775-771-4241

775-858-5952

